Quality Definition of Done v2: What the Evidence Keeps, Changes and Adds

Revises the WIP Quality DoD (Confluence 4048715783) | QA Architecture | 25 October 2026

Why the DoD must change

+49%

P1/P2 customer-found bugs

96%

of P1 incidents found by customers

Few

DoD items block today; most are policy

1.1-10.4

incidents per bug across teams


Principle

A gate blocks only where data proves the risk.

Everything else is policy or a suggested means, measured and reviewed.

Tiers come from evidence (impact, failure type, hotspot code), not from product names.

Gate map v2: where each check sits and whether it blocks

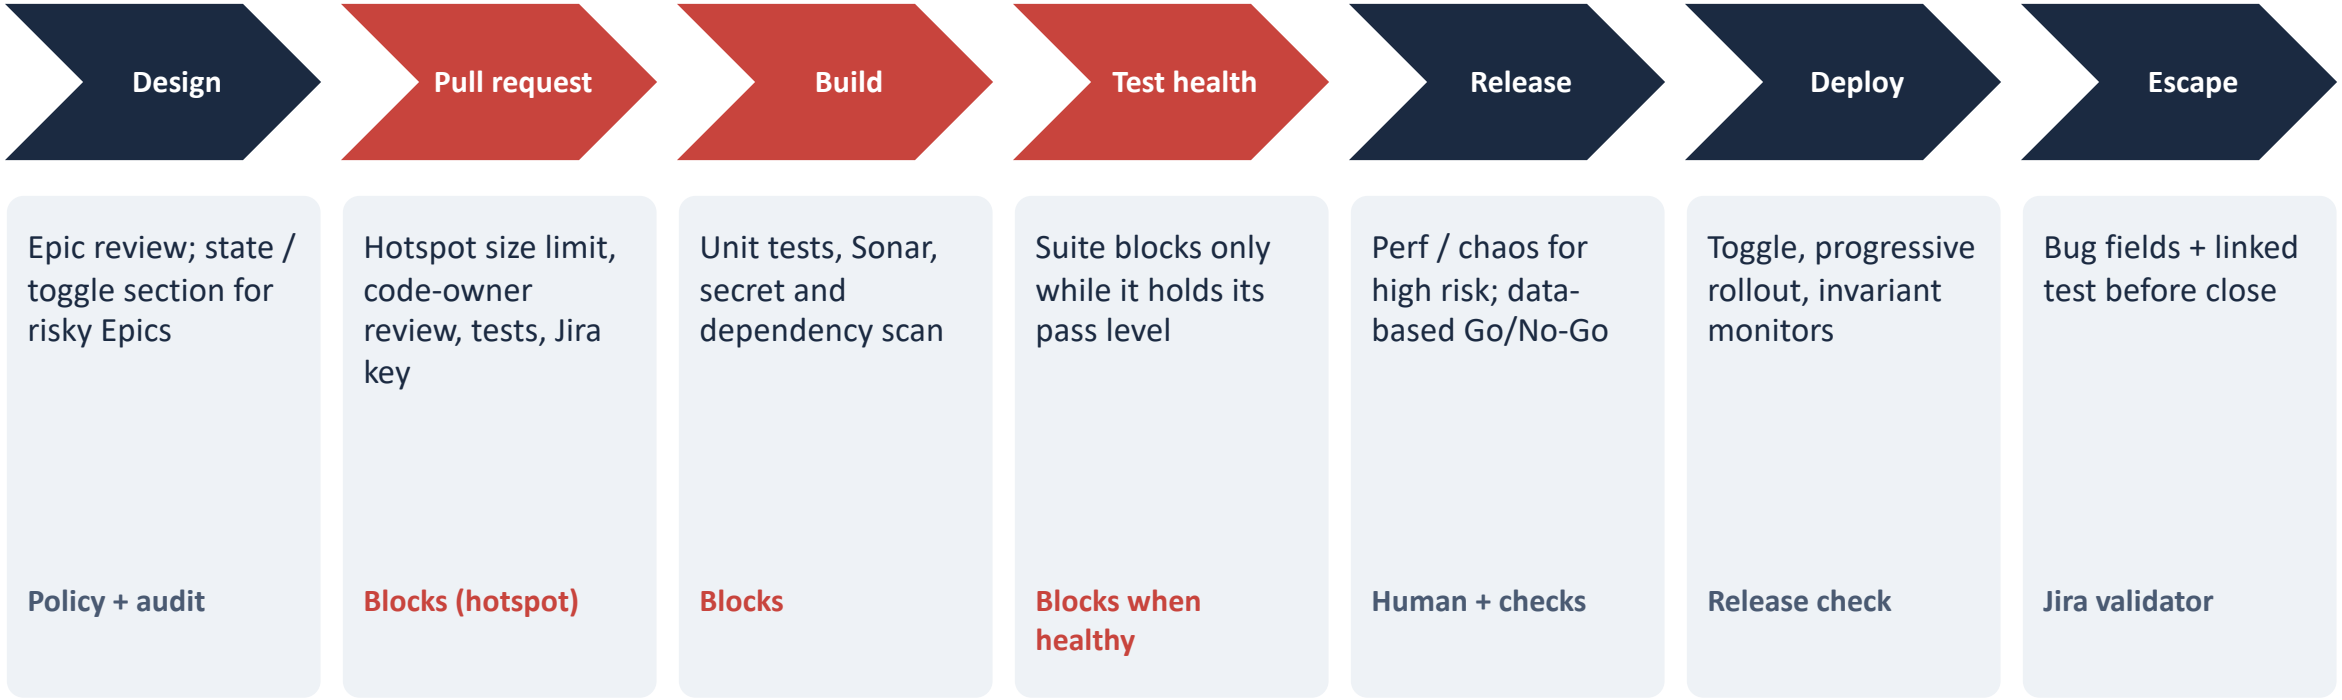

Red = blocks. Agents (test plan, Playwright, RIA, exploratory, mutation) feed these checks; they are not gates by themselves.

Epic level: your WIP items, verdict by evidence

WIP DoD item	v2 verdict	Enforcement	Evidence
PRD / Epic review, acceptance criteria	**Strengthen: risky Epics**	Jira flow + audit	Causing stories link a spec 6.8% vs 31.8%
RIA phase 1 / phase 2	**Change: fixes + hotspots**	Policy; phase 2 later	RIA miss 7-15%; half had RIA done
Test plan / Playwright generator	**Keep: as means**	Suggested	No escape evidence yet
SonarQube gate	**Keep: block everywhere**	Required CI check	Required in 1 of 5 pilot repos
Mutation >= 80% (blocking)	**Change: visible first**	Block per scope later	Weak tests 3%; 2 of 4 fails false
ReportPortal; pipeline stable	**Change: test health**	Blocks when healthy	Routing E2E 1.2% pass
Performance test, Chaos Runner	**Keep: high risk only**	Release check	Race / scale escapes 13-23%
All tests in Xray, linked	**Change: escape + risky**	Policy + audit	Links 18-25% today
Plan reviewed with PM / Architect, PO	**Keep: high-impact teams**	Policy	Teams differ strongly

Release level: your WIP items, verdict by evidence

WIP DoD item	v2 verdict	Enforcement	Evidence
Feature toggle registered, owner, removal	**Keep: mandatory**	Release check	Monolith cannot roll back
Toggle verified on and off	**Keep: high risk**	Release check	Same
Deploy and rollback verified	**Change: toggle-off + progressive**	Release check	Rollback not possible on monolith
Post-deploy sanity by toggle	**Keep**	Release check	-
Synthetic monitor for changed paths	**Strengthen: correctness monitors**	Release check (high risk)	96% of P1 found by customers
No open P1-P3	**Keep**	Go/No-Go	-
Go/No-Go sign-off	**Change: data-based**	Human + data	26.4 pages mostly TBD

New items the evidence adds

New item	v2 verdict	Enforcement	Evidence
Intake: defect vs MI vs expectation gap	**Add**	Jira required field	MI tickets inflated the 2026 rise
Bug fields: type, detected-by, cause	**Add**	Jira required (X1)	Cause known for ~25% only
Escape-to-test before close	**Add**	Jira validator	38% of RCAs add a test today
Hotspot PR rules: size, owner, tests	**Add**	Blocks on hotspot paths	Follow-up fixes 21% -> 54% by size
CODEOWNERS for hotspot code	**Add**	Required review	Monolith has none; bus factor 1
Bug-fix review, correctness types	**Add**	Policy -> block if X4	1 in 4 known causes is a fix
Emergency-change follow-up review	**Add**	Policy	Emergency changes x2.9 since June

Tiers by evidence, not by product name

High risk

Assigned by

- High-impact team type
- Correctness-critical failure types (routing, contact lifecycle, report data, agent state)
- Hotspot code

Gets

- All blocking checks
- Perf and chaos stage
- Invariant monitors
- Plan review with PM / Architect

Standard

Assigned by

- All other teams and code

Gets

- Common baseline (intake, fields, RCA)
- Sonar + test health
- Feature toggles

When the DoD v2 takes effect

Now

- Bug intake rule and fields
- Sonar required in every repo
- Mutation score visible in Sonar
- Go/No-Go with data
- Triage routing E2E failures

Q1 2027

- Hotspot PR rules (X3)
- Bug-fix review (X4)
- Correctness monitors in shadow (X2)
- CODEOWNERS for hotspots

April 2027

- Results vs control teams
- Decide which checks block, per tier
- Mutation blocking per scope, if proven
- Harness only for proven checks
